

Work Order ID 143405

Tuesday, March 15, 2016 11:45:56 AM

143405

Page 1

Item ID: D5149-041W

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Step Base Assembly Weldment

Start Date: 5/5/2016 Start Qty: 12.00

12

Cust Item ID:

Required Date: 5/13/2016 Req'd Qty: 12.00

12

Customer:

Reference:

Approvals: Process Plan: MCS Date: MAR 17 2016

Tooling:

Date:

Run Start ***NR1***

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D5149	D								
110	Weld per dwg A/R Aluminum rod Batch: _____	0.00							
110									
Large Fab	Memo	0.11							
Large Fab	USE DT10134 WELDING FIXTURE TO WELD D5149-041								
120	QC9- Inspect visual per QSI004- Fusion Welds	0.00							
120									
QC	Memo	0.00							
Quality Control									
130	QC5- Inspect part completeness to step on W/O	0.00							
130									
QC	Memo	0.00							
Quality Control									

12

16-07-06
JML

9

16-07-07

DAS
9
9-88

12

16-07-07

DAS
9
9-88

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY																																																											
☐ Environment	☐ Design	☐ Doc/Data	☐ Equip/Tooling	☐ Handling/Pre	☐ Material	☐ Internal Transport	☐ Tribal Knowledge	☐ LOA	☐ Substation	☐ Past Expiry Date	☐ Misidentified	☐ No Re-verification	☐ Operator	☐ Offset/Setup	☐ Supplier	☐ Training	☐ Use for Testing	☐ Poor Information	☐ Rushing	☐ Product Improvement	☐ Process Improvement	☐ Manufacturing Process	☐ Past Due	☐ Pressure/Forced	☐ Bending	☐ Centre Not Concentric	☐ Cracks	☐ Crimp/Kink/Ripple/Wave	☐ Cuffs	☐ Crushing	☐ Heat Treat	☐ Wave/Twist in Tube	☐ Marks/Chatter	☐ Temperature/Cure	☐ Set-up	☐ BOM/Route	☐ Broken/Damage/Defect	☐ Inspection Incomplete/Unqualified	☐ Contamination	☐ Countersink	☐ Cut Too Short	☐ Instructions Incomplete/Unclear	☐ Drill Holes	☐ Power Loss/Surge	☐ Folio/Program	☐ Grain	☐ Weld	☐ Wrong Stock Pulled	☐ Out of Sequence	☐ Off-set	☐ Mislabeled	☐ Fit/Function	☐ Misaligned/off center	☐ Positioned Wrong	☐ Outside Dimensions	☐ Over/Under tolerance	☐ Part Incorrect	☐ Part Lost/Missing	☐ Part Moved	☐ Drawing	☐ Finish	☐ Misread	☐ Turning Sequence
																								OTHER: _____																																							

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY																																																											
☐ Environment	☐ Design	☐ Doc/Data	☐ Equip/Tooling	☐ Handling/Pre	☐ Material	☐ Internal Transport	☐ Tribal Knowledge	☐ LOA	☐ Substation	☐ Past Expiry Date	☐ Misidentified	☐ No Re-verification	☐ Operator	☐ Offset/Setup	☐ Supplier	☐ Training	☐ Use for Testing	☐ Poor Information	☐ Rushing	☐ Product Improvement	☐ Process Improvement	☐ Manufacturing Process	☐ Past Due	☐ Pressure/Forced	☐ Bending	☐ Centre Not Concentric	☐ Cracks	☐ Crimp/Kink/Ripple/Wave	☐ Cuffs	☐ Crushing	☐ Heat Treat	☐ Wave/Twist in Tube	☐ Marks/Chatter	☐ Temperature/Cure	☐ Set-up	☐ BOM/Route	☐ Broken/Damage/Defect	☐ Inspection Incomplete/Unqualified	☐ Contamination	☐ Countersink	☐ Cut Too Short	☐ Instructions Incomplete/Unclear	☐ Drill Holes	☐ Power Loss/Surge	☐ Folio/Program	☐ Grain	☐ Weld	☐ Wrong Stock Pulled	☐ Out of Sequence	☐ Off-set	☐ Mislabeled	☐ Fit/Function	☐ Misaligned/off center	☐ Positioned Wrong	☐ Outside Dimensions	☐ Over/Under tolerance	☐ Part Incorrect	☐ Part Lost/Missing	☐ Part Moved	☐ Drawing	☐ Finish	☐ Misread	☐ Turning Sequence
																								OTHER : _____																																							

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐			FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		
OTHER : ☐					

Work Order ID 143405***143405***

Page 4

Tuesday, March 15, 2016 11:45:56 AM

Item ID: D5149-041W

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Step Base Assembly Weldment

Start Date: 5/5/2016 Start Qty: 12.00

12

Cust Item ID:

Required Date: 5/13/2016 Req'd Qty: 12.00

12

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
200	Identify as per dwg & Stock Location: _____	0.00							
200									
Packaging	Memo	0.00							
Packaging	LOCATION : GA								
210	QC21- Final Inspection - Work Order Release	0.00							
210									
QC	Memo	0.02							
Quality Control									

JUL 13 2016

DAS
6
3-29

16/7/13

DAS
21
3-29

JUL 13 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="border: none;">Skid-tube ☐</td> <td style="border: none;">Cross tube ☐</td> <td style="border: none;">Water Jet ☐</td> <td style="border: none;">Engineering ☐</td> </tr> <tr> <td style="border: none;">Machining ☐</td> <td style="border: none;">Small Fab ☐</td> <td style="border: none;">Prod. Eng. Coord. ☐</td> <td style="border: none;">Quality ☐</td> </tr> <tr> <td style="border: none;">Thermoforming ☐</td> <td style="border: none;">Finishing ☐</td> <td style="border: none;">Rec/Store/Packaging ☐</td> <td style="border: none;">Other ☐</td> </tr> <tr> <td style="border: none;">Large Fab ☐</td> <td style="border: none;">Composite ☐</td> <td style="border: none;">Supplier ☐</td> <td></td> </tr> </table>				Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																		
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																		
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																		
Large Fab ☐	Composite ☐	Supplier ☐																			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval																	
Description Work Order Deviation			Disposition																		
			Completed By																		
			Lead hand / Supervisor Approval Verification																		
			QC / QA Coordinator Approval																		
Root Cause		FAULT CATEGORY																			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐																
OTHER : ☐																					

Picklist Print

Tuesday, March 15, 2016 11:45:55 AM

Page 1

Work Order ID: 143405

143405

Parent Item: D5149-041W

D5149-041W

Parent Item Name: Fwd Step Base Assembly Weldment

Start Date: 5/5/2016

Required Date: 5/13/2016

Start Qty: 12.00

Required Qty: 12.00

Comments: IPP REV:A 14.12.15 NEW ISSUE DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D5149-1		Manufactured	No				Each	9.0000		12			
D5149-1									**				
Fwd Step Base													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				WA004	143429			9		127			
					140117			9					
D5149-3		Manufactured	No				Each	9.0000		12			
D5149-3									**				
Fwd Step													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				WA001	143487			9		12			
					139079			9					
D5149-5		Manufactured	No				Each	52.0000		12			
D5149-5									**				
Step Cap													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				WA001	145680			52		17			
					129795			6					
					137148			2					
					140103			44		15			

16-07-05
JLM

16-07-05
JLM

16-07-05
JLM

DQA: _____ Date: _____





WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					

ITEM	QTY -041	P/N	DESCRIPTION
	X	D5149-041	FWD STEP ASSEMBLY
1	1	D5149-041W	FWD STEP BASE WELDMENT
2	1	D5151-1	CLAMP CUSHION

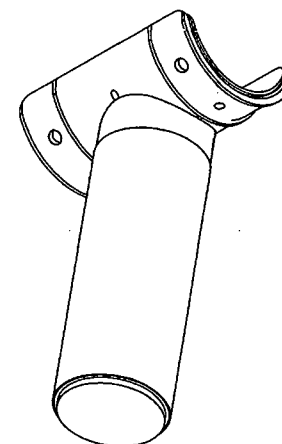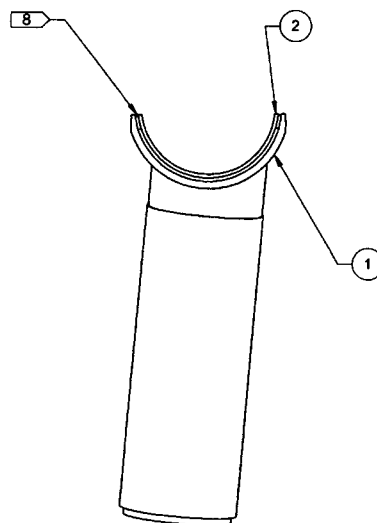

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 143405 MC

16-03-17

D5149-041 FWD STEP ASSEMBLY



NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.1
- 7) WEIGHT: 0.69 lbs
- 8) BOND D5151-1 CUSHION TO D5149-041W BASE WELDMENT USING 3M 1300L ADHESIVE

D	DIAMETER OF D5149-5 CAP IS NOW 1.88 WAS 2.00 TO EASE WELDING PROCEDURE, UPDATE TOLERANCES	AP	15.10.20
C	ANTISKID FINISH DIM MODIFIED DUE TO INTERFERENCE WITH WELD (SHT 3 & 4)	AP	15.04.27
B	COMPLETE RE-DESIGN, SEE PREVIOUS REV FOR DETAILS	DB	15.01.14
A	NEW ISSUE	DB	14.10.25
REV.	DESCRIPTION	BY	DATE
DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 1 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASED
2015-11-04
EN 15-142

ITEM	QTY -043	P/N	DESCRIPTION
	X	D5149-043	AFT STEP ASSEMBLY
1	1	D5149-043W	AFT STEP BASE WELDMENT
2	1	D5151-3	CLAMP CUSHION

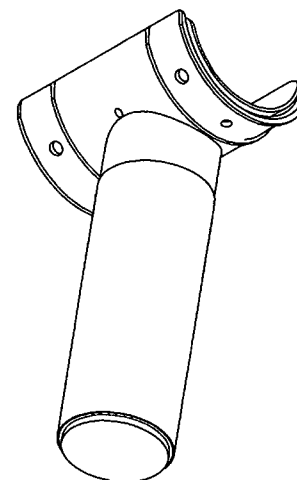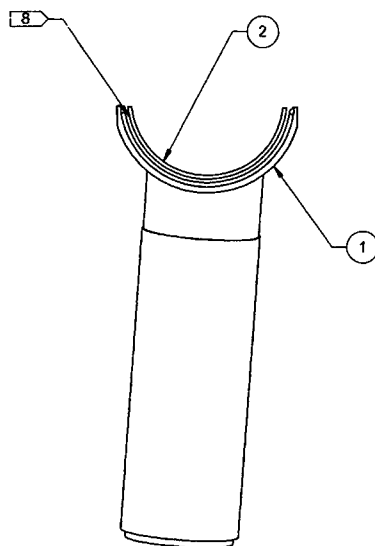

D5149-043 AFT STEP ASSEMBLY

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.1
- 7) WEIGHT: 0.87 lbs
- 8) BOND D5151-3 CUSHION TO D5149-043W BASE WELDMENT USING 3M 1300L ADHESIVE

RELEASED
2015-11-04
CS

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 2 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

ITEM	QTY-041W	P/N	DESCRIPTION
	X	D5149-041W	FWD STEP BASE WELDMENT
1	1	D5149-1	FWD STEP BASE
2	1	D5149-3	FWD STEP
3	1	D5149-5	STEP CAP

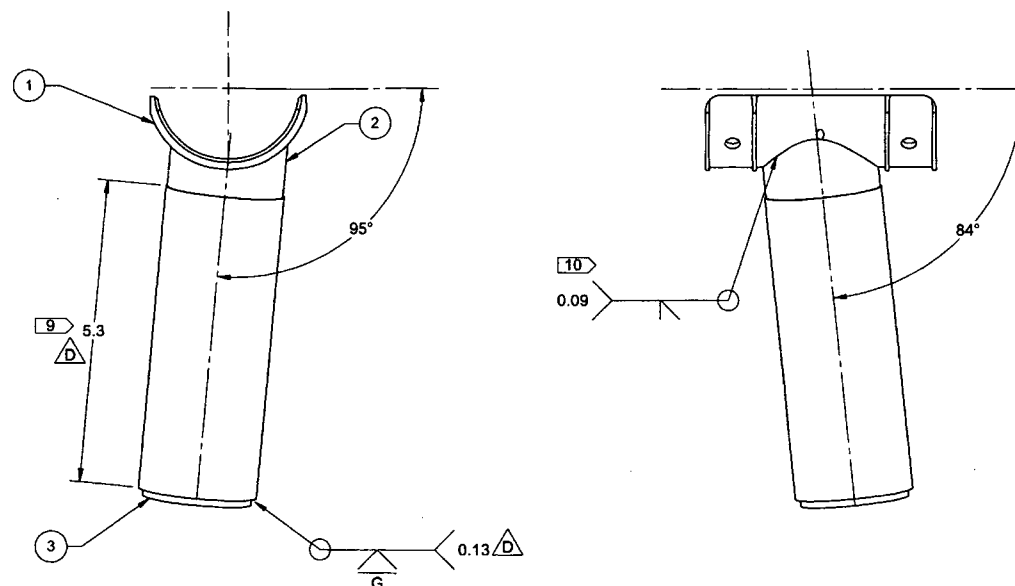

D5149-041W FWD STEP BASE WELDMENT

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "WHITE" (4.3.5.1) PER DART QSI 005 4.3
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.67 lbs
- 8) WELDING PER DART QSI 004
- 9) APPLY BLACK ANTI-SKID PAINT TO STEP TUBE, ALL AROUND PER DART QSI 005 4.4
- 10) ALIGN D5149-3 FWD STEP WITH EDGE OF ALIGNMENT HOLES IN D5149-1 FWD STEP BASE PRIOR TO WELDING

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 3 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

ITEM	QTY- 043W	P/N	DESCRIPTION
	X	D5149-043W	AFT STEP BASE WELDMENT
1	1	D5149-5	STEP CAP
2	1	D5149-7	AFT STEP BASE
3	1	D5149-9	AFT STEP

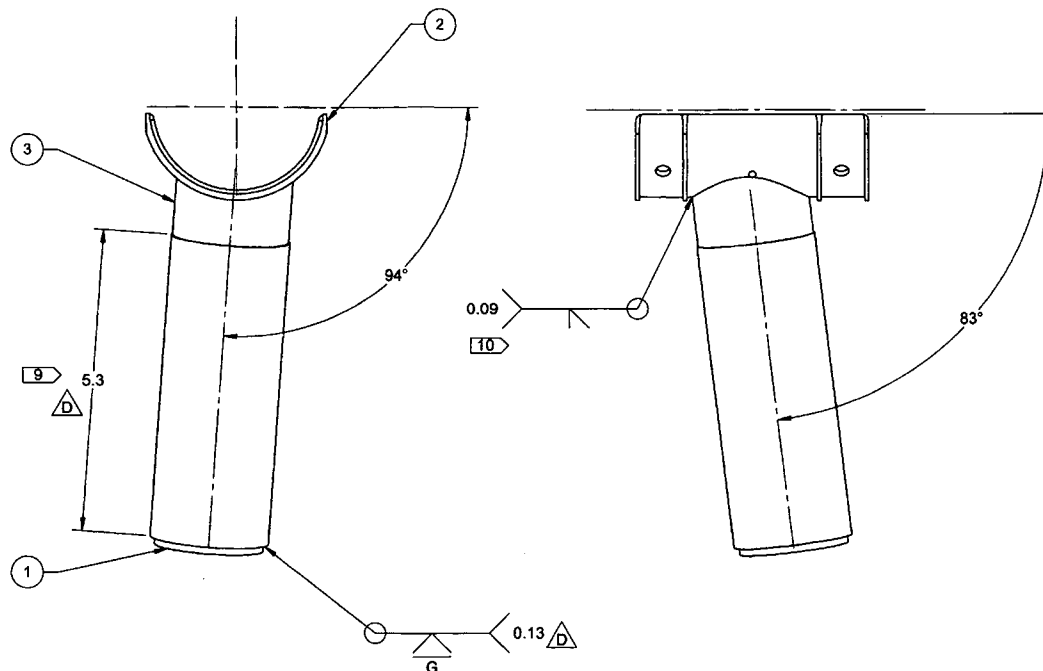

D5149-043W AFT STEP BASE WELDMENT


NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
POWDER COAT "WHITE" (4.3.5.1) PER DART QSI 005 4.3
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.67 lbs
- 8) WELDING PER DART QSI 004
- 9) APPLY BLACK ANTI-SKID PAINT TO STEP TUBE, ALL AROUND PER DART QSI 005 4.4
- 10) ALIGN D5149-9 AFT STEP WITH EDGE OF ALIGNMENT HOLES IN D5149-7 AFT STEP BASE PRIOR TO WELDING


DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 4 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

RELEASED
2015-11-04

APPROVED

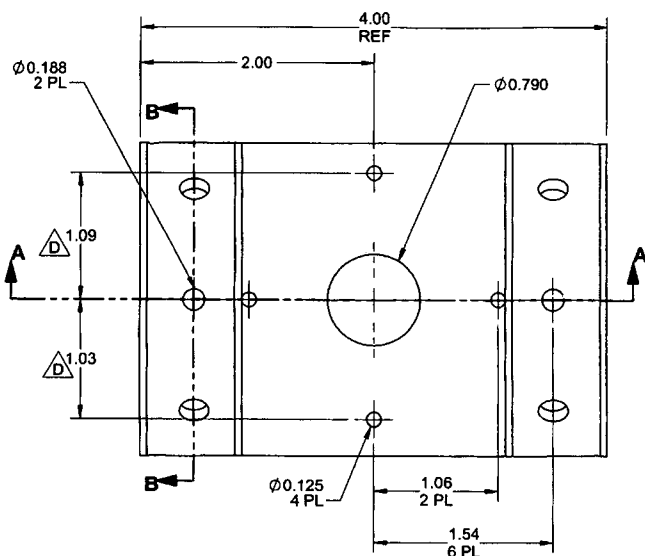

D5149-1 FWD STEP BASE
(MAKE FROM D5149-1TRN)




SECTION A-A


0.06 X 45° CMF
ALL AROUND INSIDE EDGE

NOTES:

- 1) MATERIAL: MAKE FROM D5149-1TRN
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.20 lbs

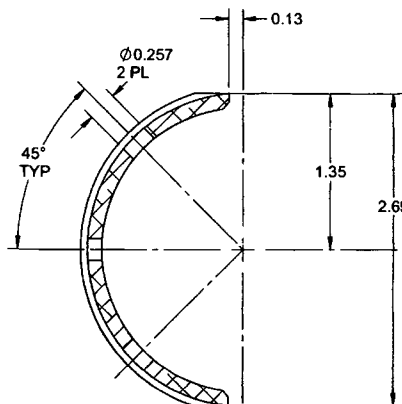


SECTION B-B
2 PL



RELEASED
2015-11-04

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 5 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

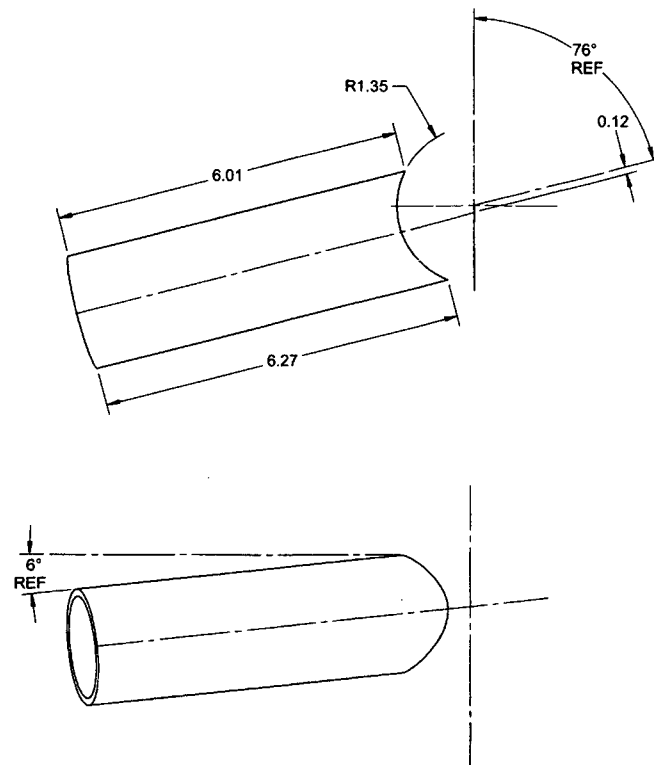

D5149-3 FWD STEP



NOTES:

- 1) MATERIAL: 6061-T6/T62/T6510/T6511 SEAMLESS TUBING PER WW-T-700/6 OR QQ-A-200/8 OR QQ-A-225/8 OR AMS 4080 OR AMS 4082 OR AMS 4083 OR ASTM B210 OR ASTM B241
REF DART SPEC M6061T6T2.000W0.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.42 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 6 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

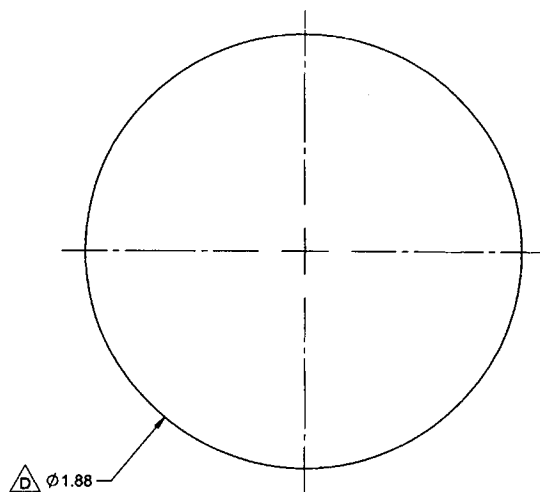

D5149-5 STEP CAP


NOTES:

- 1) MATERIAL: 6061-T6 (OR 6061-T62) ALUMINUM SHEET, 0.125 THICK
PER QQ-A-250/11 OR AMS-QQ-A-250/11 OR AMS 4025 OR AMS 4027 OR ASTM B209
REF DART SPEC M6061T6S.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.03 lbs


RELEASED
2015-11-04

APPROVED



DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	OD	D5149	SHEET 7 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

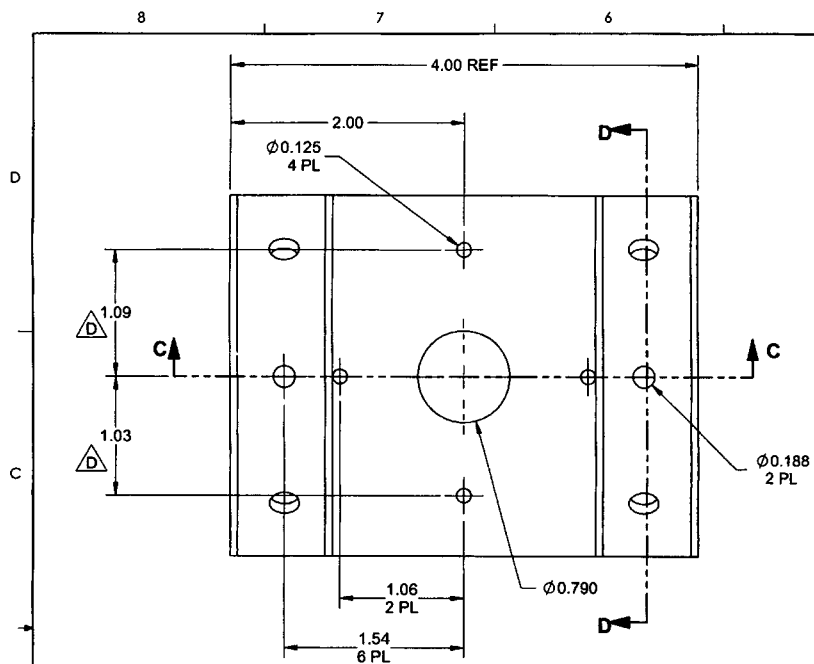

D5149-7 AFT STEP BASE
(MAKE FROM D5149-7TRN)

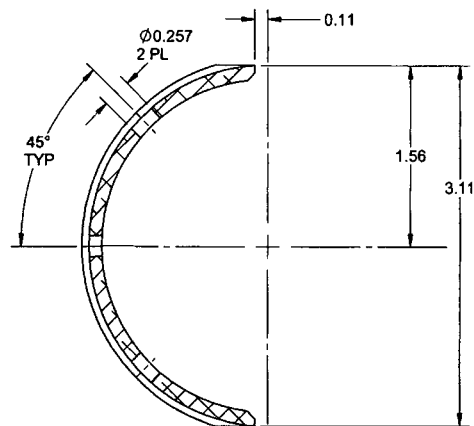

SECTION D-D
2 PL



SECTION C-C

0.06 X 45° CMF
ALL AROUND INSIDE EDGE



NOTES:

- 1) MATERIAL: MAKE FROM D5149-7TRN
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.30 lbs


RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 8 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DSC	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

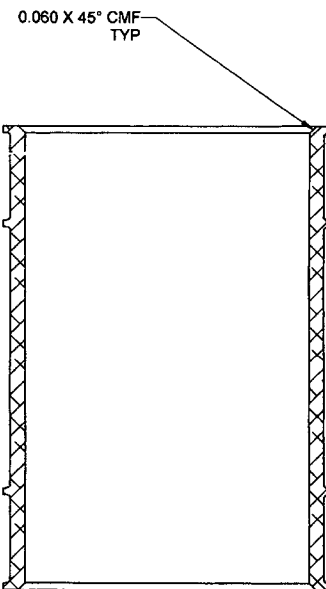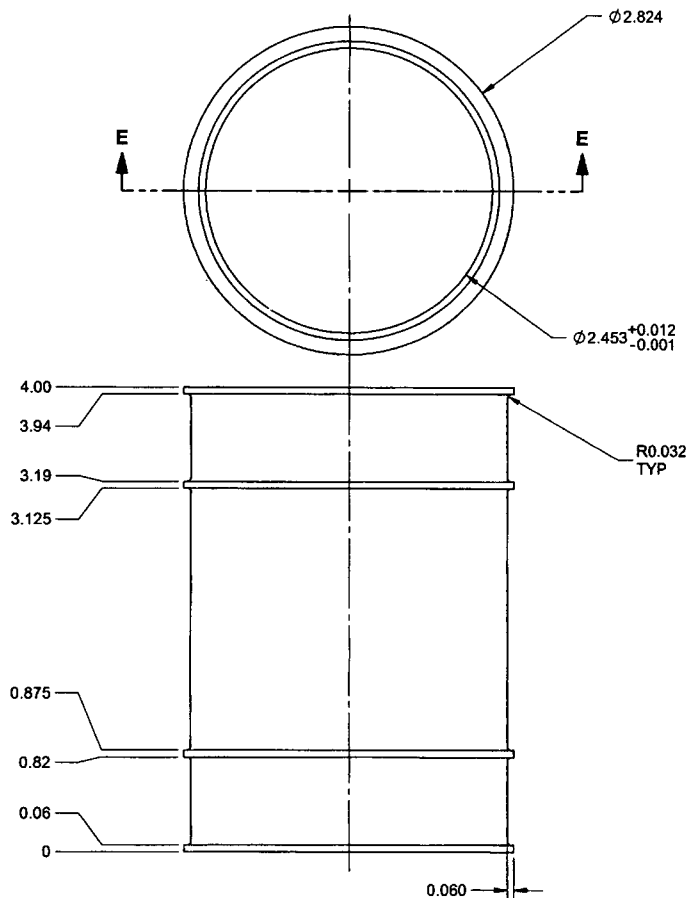

SECTION E-E



D5149-1TRN TURNING DETAIL



NOTES:

- 1) MATERIAL: 6061-T6/T651/T6510/T6511/T62 ALUMINUM ROUND BAR
PER QQ-A-225/8 OR AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116)
OR QQ-A-200/8 OR AMS-QQ-200/8 (OR AMS 4160) OR ASTM B211 OR ASTM B221
REF DART SPEC. M6061T6R
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.41 lbs


RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 9 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

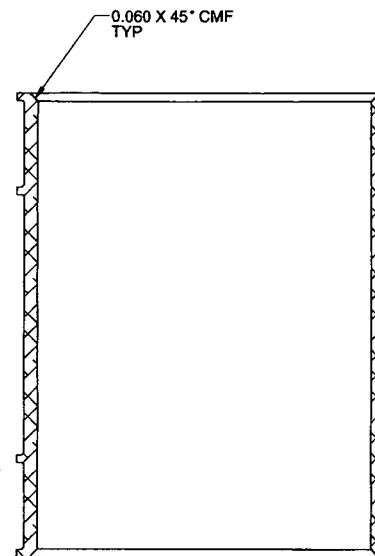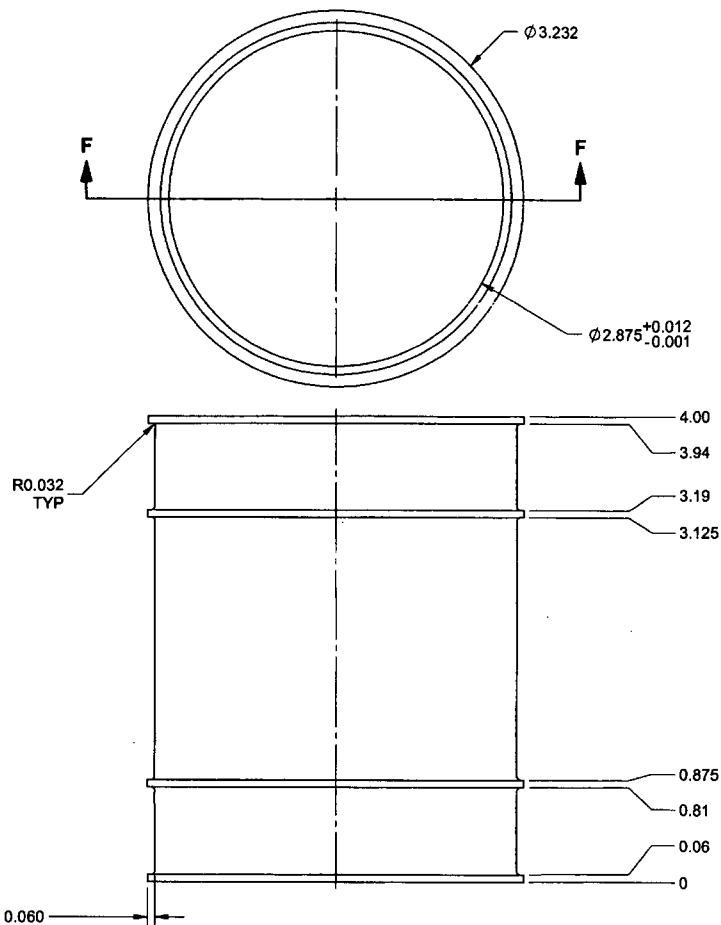

SECTION F-F



D5149-7TRN TURNING DETAIL




NOTES:

- 1) MATERIAL: 6061-T6/T651/T6510/T6511/T62 ALUMINUM ROUND BAR
PER QQ-A-225/8 OR AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116)
OR QQ-A-200/8 OR AMS-QQ-200/8 (OR AMS 4160) OR ASTM B211 OR ASTM B221
REF DART SPEC. M6061T6R
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.41 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DB	D5149	SHEET 10 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS COVENANT THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

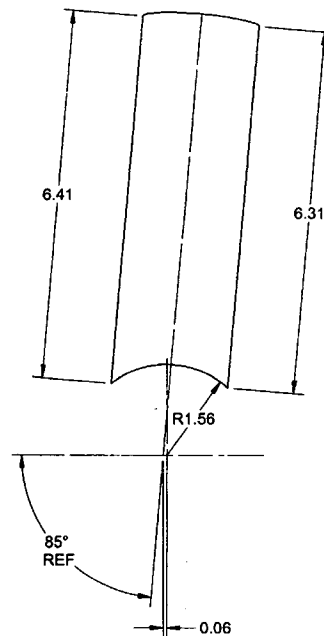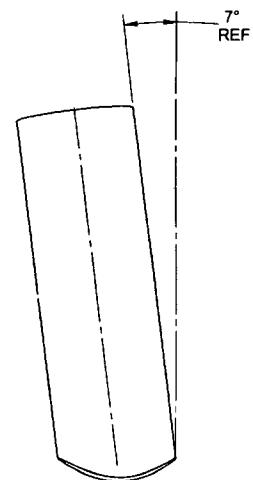

D5149-9 AFT STEP

NOTES:

- 1) MATERIAL: 6061-T6/T62/T6510/T6511 SEAMLESS TUBING PER WW-T-700/6 OR QQ-A-200/8 OR QQ-A-225/8 OR AMS 4080 OR AMS 4082 OR AMS 4083 OR ASTM B210 OR ASTM B241
REF DART SPEC M6061T6T2.000W0.125
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.44 lbs

RELEASED
2015-11-04

APPROVED

DESIGN	DB	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	DB	DRAWING NO.	REV. D
MFG. APPR.	DD	D5149	SHEET 11 OF 11
APPROVED	WM	TITLE	SCALE
DE APPR.	DS	STEP ASSEMBLY	NTS
DATE	15.10.20	COPYRIGHT © 2014 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			
